

PROJECT OBJECTIVES

- 1. INVITING & APPROACHABLE
- 2. CREATE A CLEAR CIVIC PRESENCE
- 3. COMMUNITY & SERVICE FOCUSED
- 4. EFFICIENT IN PLANNING
- 5. ALLOW FOR FUTURE EXPANSION
- 6. SAFE & SECURE
- 7. MEETS ADDITION / RENOVATION SQ FT GOALS
- 8. MEETS PROGRAM GOALS
- 9. BUILDING RE-BRANDING / UNIQUE IDENTITY
- 10. DAYLIGHTING / QUALITY OF INTERIOR SPACES































November Updates

Exterior


- Solar Arrays Completed
- Passive Security Completed
- Finished Asphalt Completed
- Parking Lot Lighting Comp.
- Multi-use Trail Completed
- Landscaping In progress
- Stonework In progress
- Security Fencing In progress

Interior

- 3rd Floor Status Punch List
- Exterior Doors In progress
- Police Locker Room In progress
- Technology Systems In progress
- Furniture Installation January Start

Schedule

• 88% Complete Based on Time

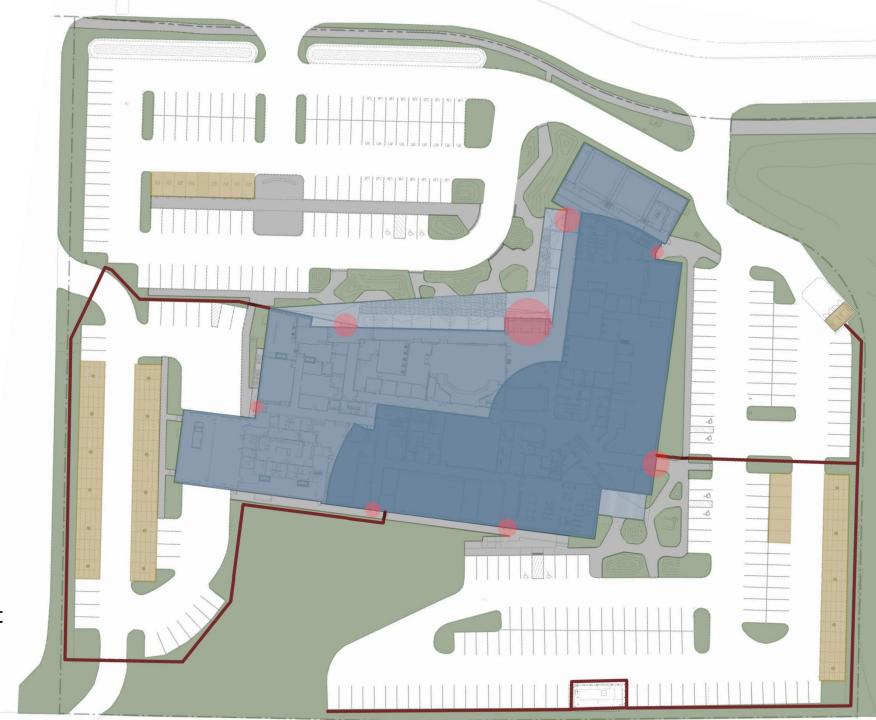





November Updates

Exterior

- Solar Arrays Completed
- Passive Security Completed
- Finished Asphalt Completed
- Parking Lot Lighting Comp.
- Multi-use Trail Completed
- Landscaping In progress
- Stonework In progress
- Security Fencing In progress

Interior

- 3rd Floor Status Punch List
- Exterior Doors In progress
- Police Locker Room In progress
- Technology Systems In progress
- Furniture Installation January Start

Schedule

• 88% Complete Based on Time























November 18, 2025






Main Lobby





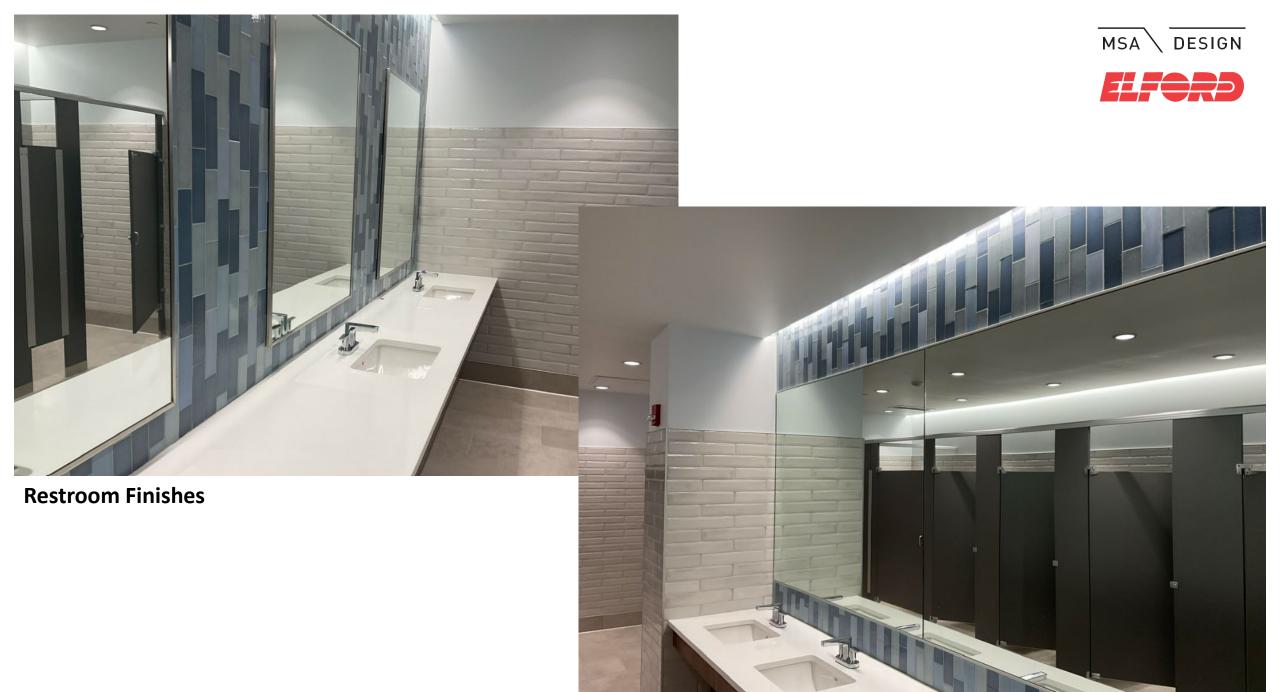





October Financial Updates

\$20,237,613
\$39,300,242
\$59,627,855
\$51,091,200

Budgeted Allowance & Contingencies	
Allowances (59%)	\$1,054,700
Contingencies (67%)	\$3,722,194
Total	\$4,776,894
Approved (65%)	\$3,113,863

