



GAHANNA CIVIC CENTER

CO-CREATE THE FUTURE

PROJECT OBJECTIVES

1. INVITING & APPROACHABLE
2. CREATE A CLEAR CIVIC PRESENCE
3. COMMUNITY & SERVICE FOCUSED
4. EFFICIENT IN PLANNING
5. ALLOW FOR FUTURE EXPANSION
6. SAFE & SECURE
7. MEETS ADDITION / RENOVATION SQ FT GOALS
8. MEETS PROGRAM GOALS
9. BUILDING RE-BRANDING / UNIQUE IDENTITY
10. DAYLIGHTING / QUALITY OF INTERIOR SPACES



GAHANNA CIVIC CENTER

CO-CREATE THE FUTURE



April 14, 2025





March Updates

Exterior

- Utility Site Work Completed
- Main Roof Top Units (HVAC) Set
- Rough Site Grading Underway

Interior


- Drywall Finishing – 2nd & 3rd Floor
- Technology CAT Cabling – 2nd & 3rd Floor
- Shaft Wall Reconstruction Complete
- Holding Facility Masonry Ongoing
- In-wall & Overhead Rough in – 1st Floor

Upcoming

- Furniture Procurement RFP (May 26)
- Moving & Logistics RFP (May 26)

Schedule

- 61% Complete Based on Time
- 24 Weather Days

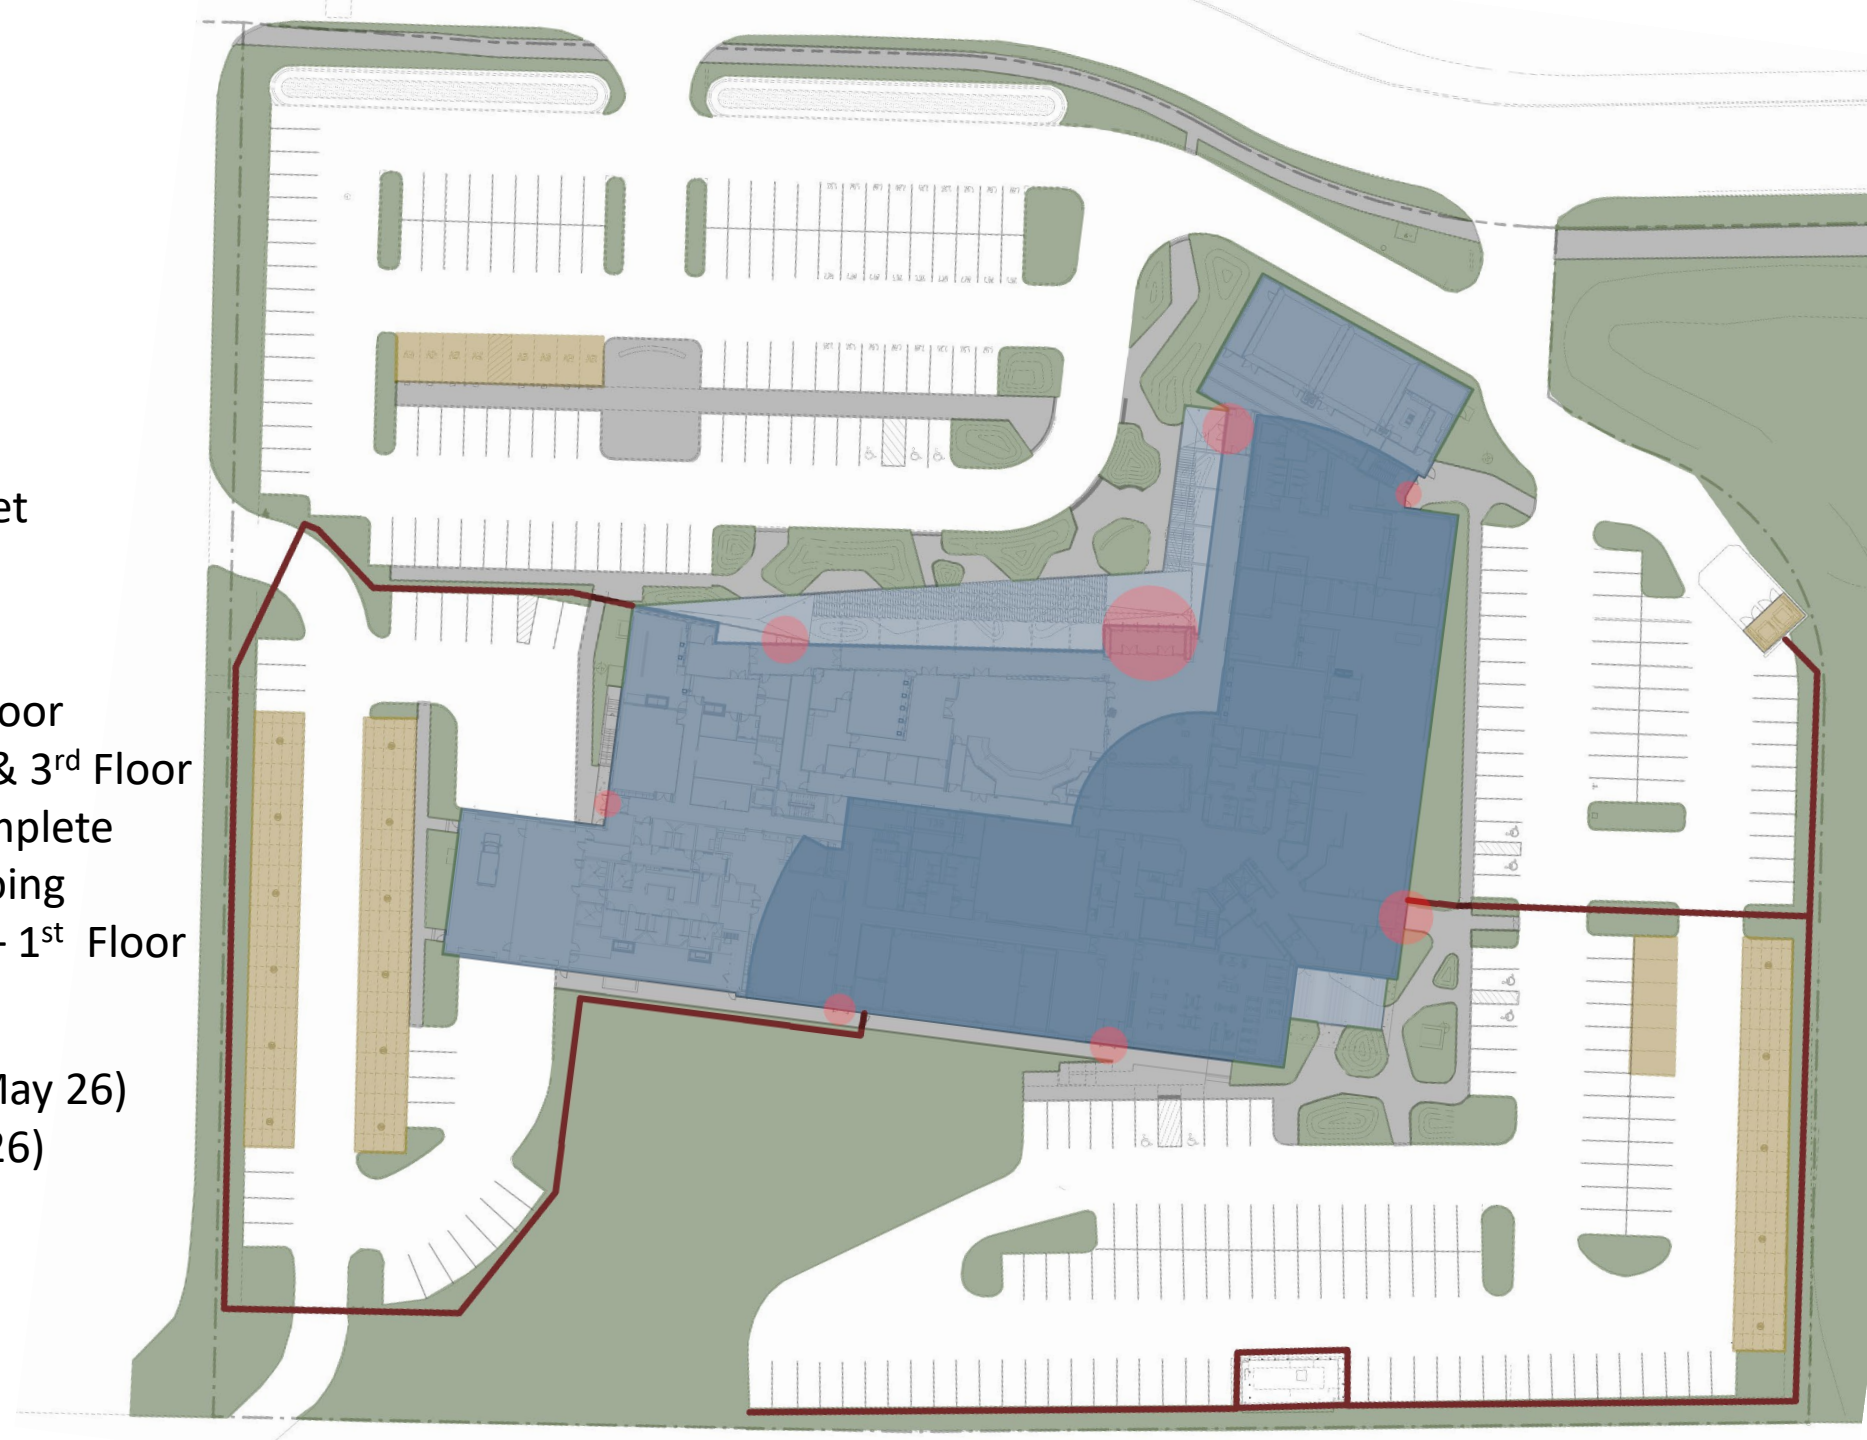

March Updates

Exterior

- Utility Site Work Completed
- Main Roof Top Units (HVAC) Set
- Rough Site Grading Underway

Interior

- Drywall Finishing – 2nd & 3rd Floor
- Technology CAT Cabling – 2nd & 3rd Floor
- Shaft Wall Reconstruction Complete
- Holding Facility Masonry Ongoing
- In-wall & Overhead Rough in – 1st Floor

Upcoming

- Furniture Procurement RFP (May 26)
- Moving & Logistics RFP (May 26)

Schedule


- 61% Complete Based on Time
- 24 Weather Days






Gahanna

MSA DESIGN
ELFORD

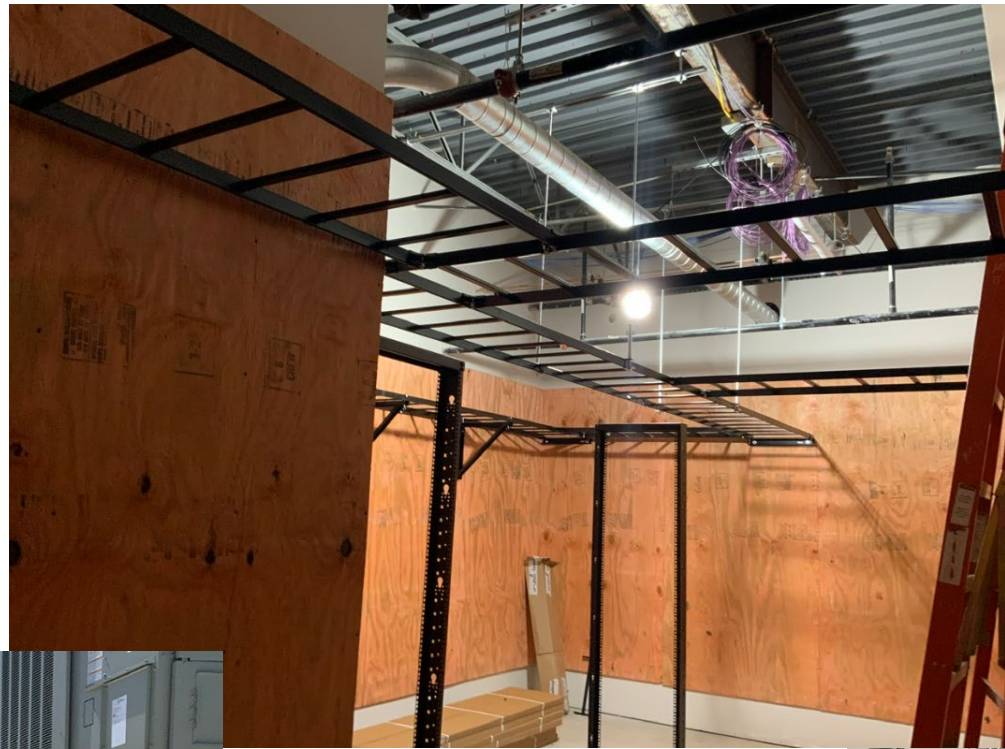


March Financial Updates

Summary

GMP1	\$20,237,613
GMP2	\$39,300,242
Total	\$59,627,855
Invoiced (46%)	\$27,485,307

Budgeted Allowance & Contingencies


Allowances (23.6%)	\$1,054,700
Contingencies (27.49%)	\$3,722,194
Total	\$4,776,894
Approved (26.6%)	\$867.943

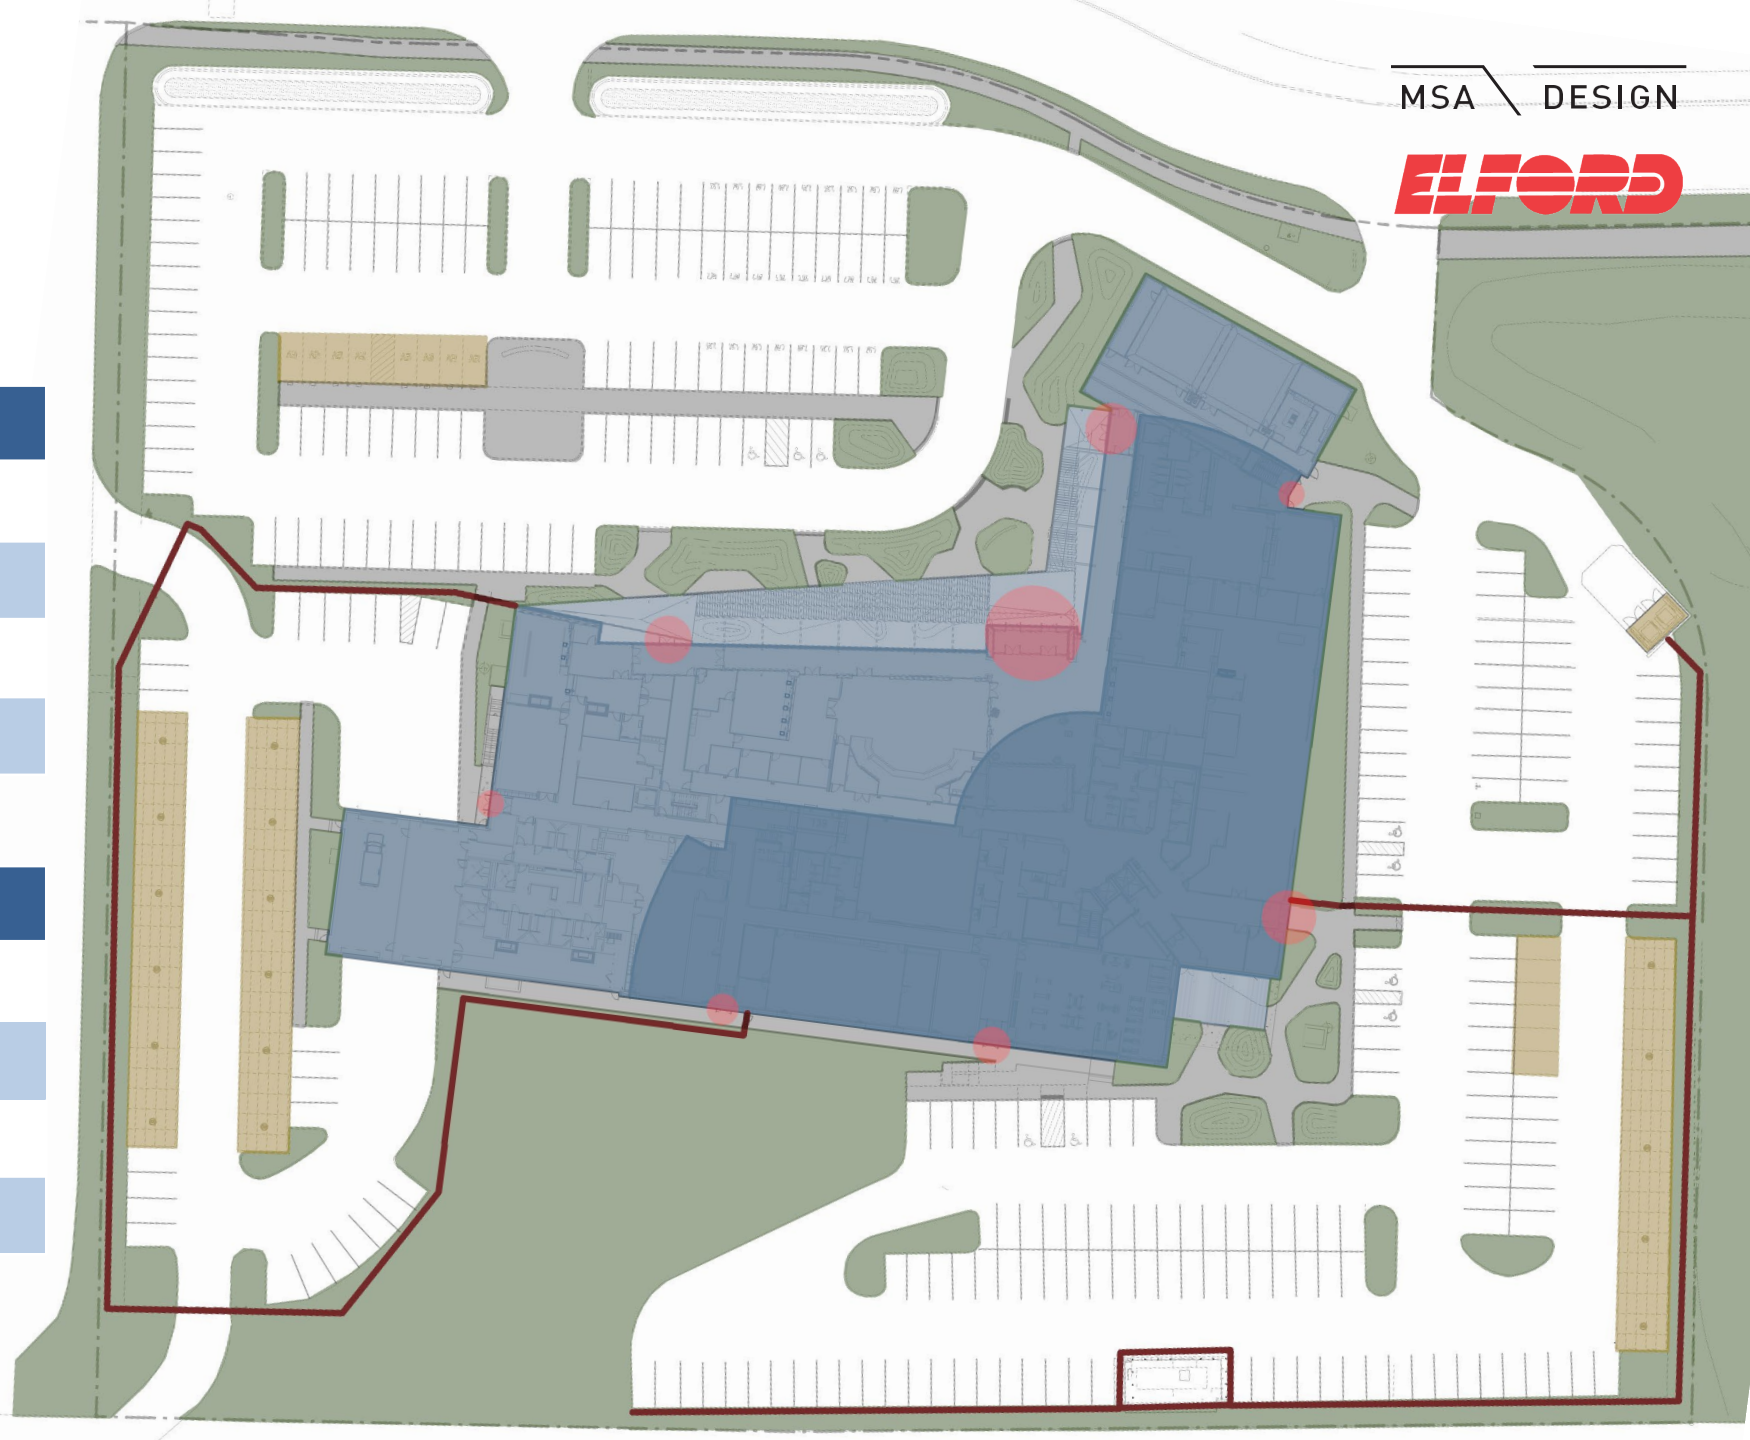

Construction Only				
	GMP1	GMP2	Total	
Construction Cost	16,799,266	34,409,406	51,208,672	
Allowances	520,000	534,700	1,054,700	2%
Construction Contingency	346,385	698,882	1,045,267	2%
Owner Contingency	346,385	2,330,542	2,676,927	4%
CM Staff & General Conditions	1,608,929	-	1,608,929	3%
CM Fees	393,397	724,896	1,118,293	2%
General Insurance	162,621	314,402	477,023	1%
Bond	142,293	275,102	417,395	1%
Commercial Activity Tax	8,337	12,312	20,649	
	20,327,613	39,300,242	59,627,855	


825 Project Summary

Building Purchase	8,500,000
Design & Preconstruction Costs	2,368,236
Construction Costs & Fees	59,627,855
Furniture, Fixtures & Equipment	1,643,216
Health & Wellness Refund (to FFE)	500,000
Third-Party Inspection	104,613
Builders Risk Insurance	57,140
Permits & Inspections	60,000
Access Easement	12,250
Land Acquisition (2 Acres)	169,406
	73,042,716

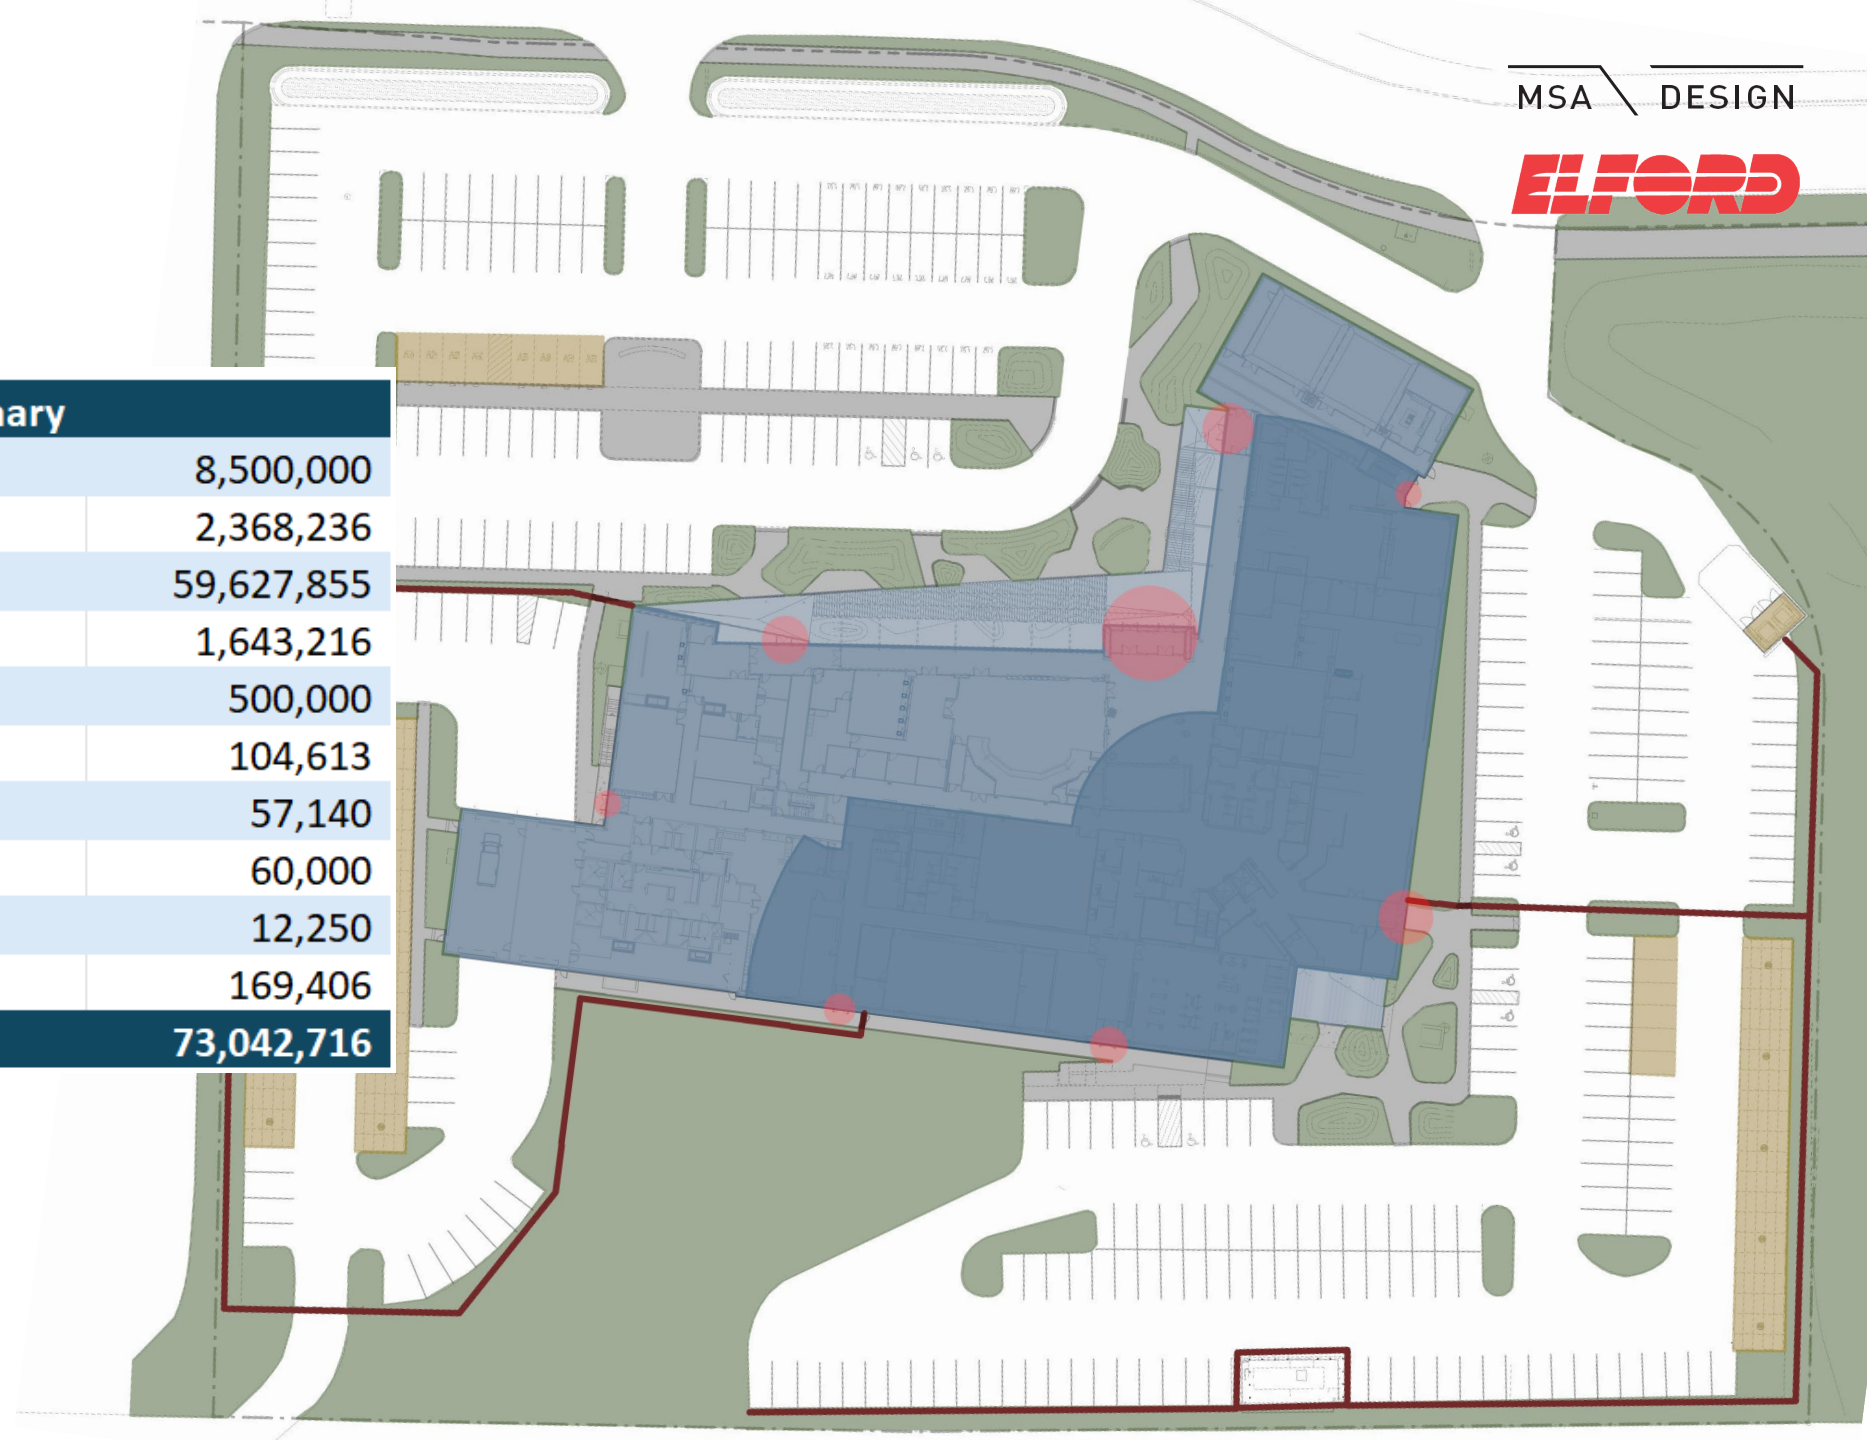

Financing

Prior Year Cash	3,350,038
Design, Downpayments, Other Expenses Above	
Building Purchase	8,500,000
Notes Rolled into Bond Issuance 1	
Bond Issuance 1	18,265,000
Less the 2012 Bond Refund & Building Purchase	
Bond Issuance 2	33,500,000
June Issuance	
Capital Fund Cash	3,000,000
Used for FFE & Contingency	
General Fund Cash	7,000,000
Used for FFE & Contingency	
73,615,038	

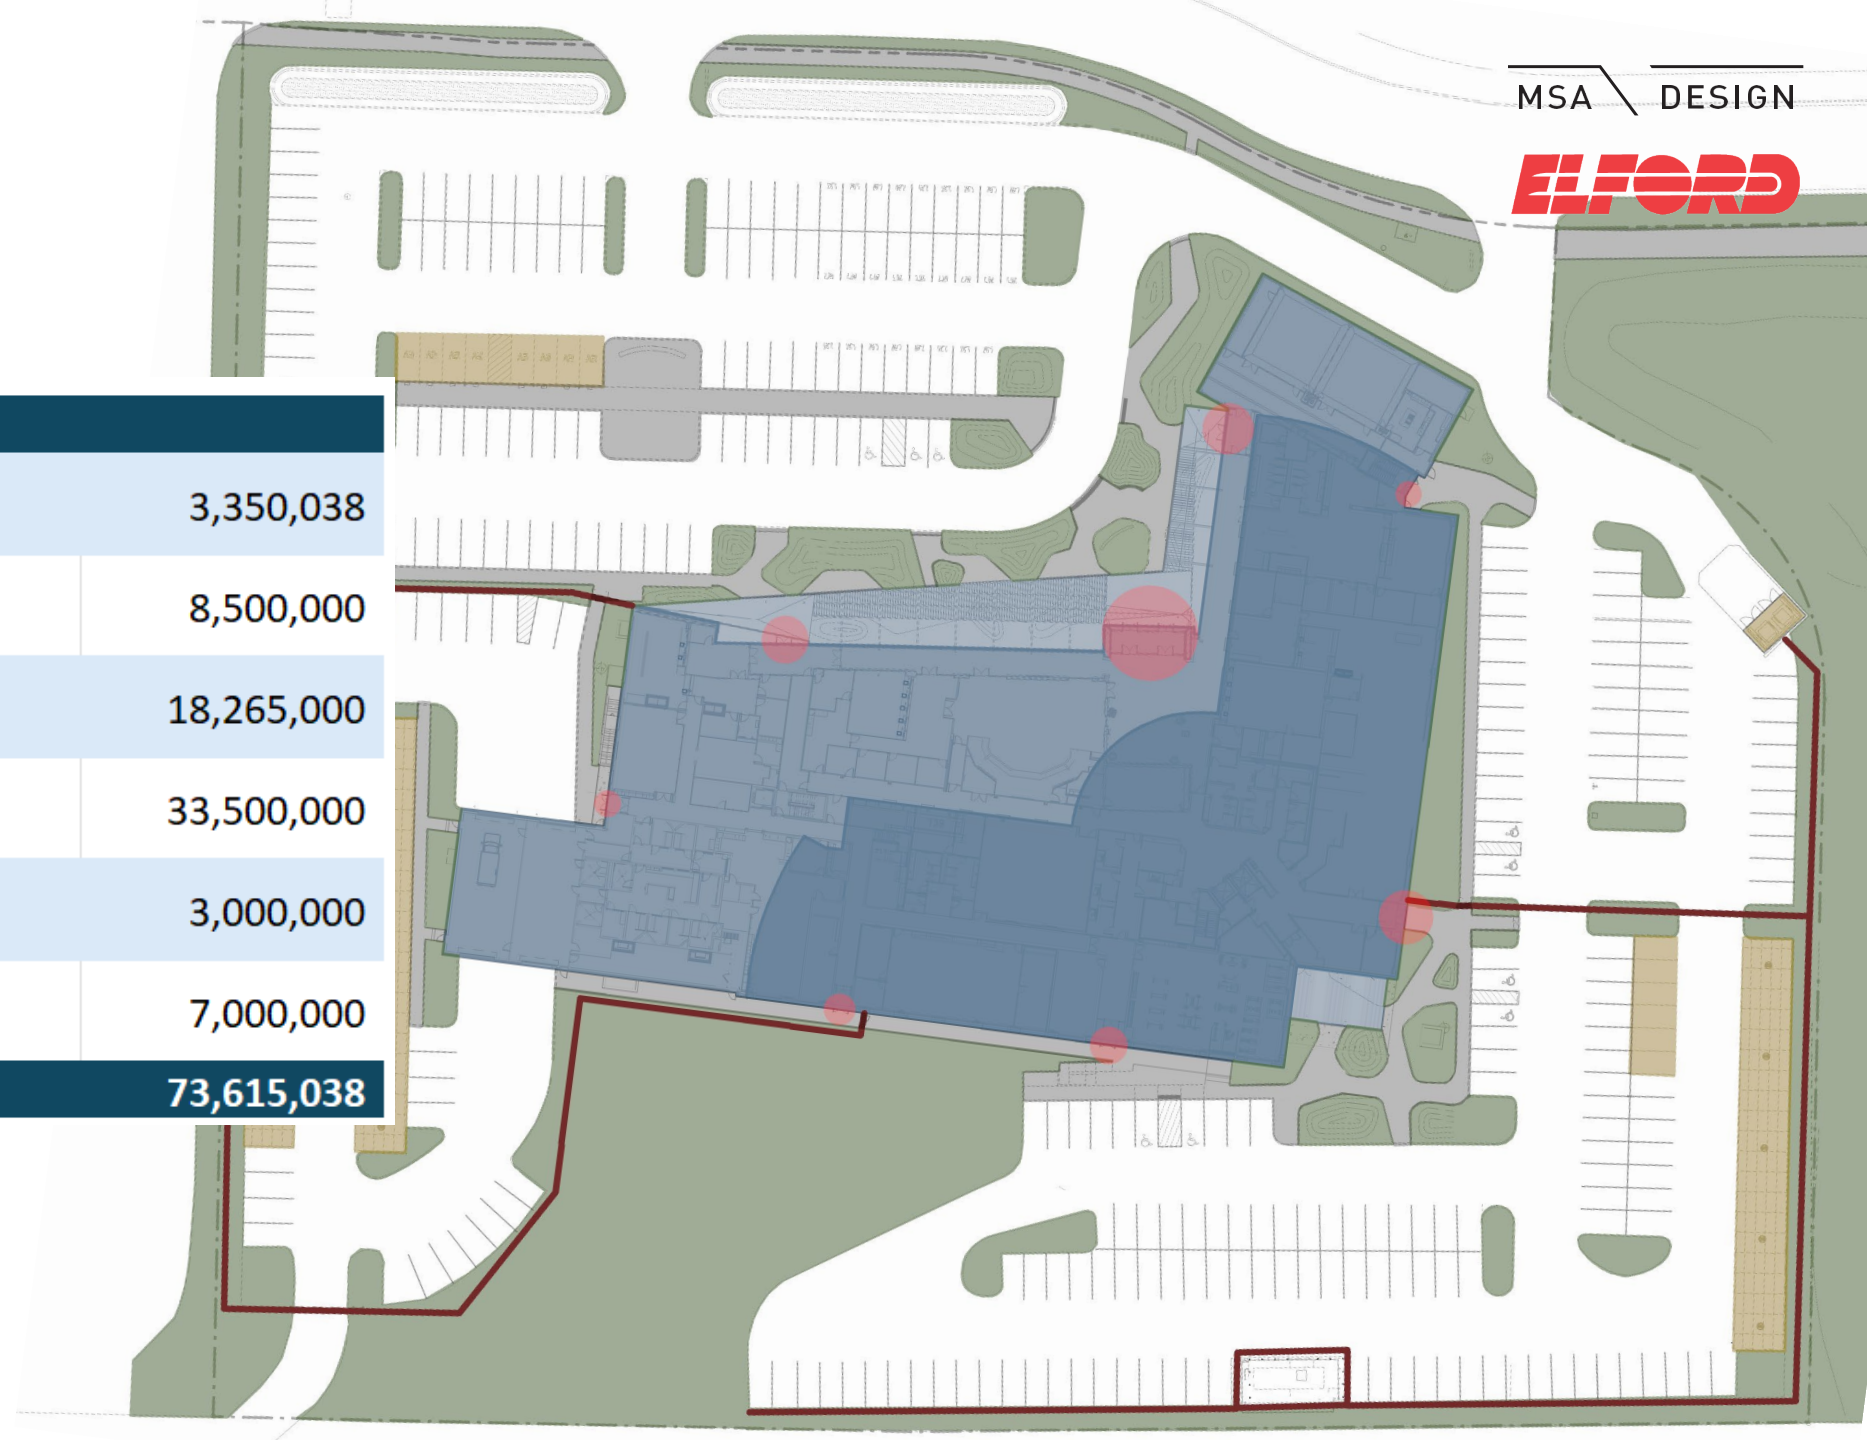



Considerations

- Public Safety Considerations
- Staff Monitoring
- Member Conversations
- Comparable Facilities
- Cost
- Aesthetics

Alternatives

- Natural Landscape Canopy

Rough Order of Magnitude

- \$300k - \$350k

MSA DESIGN





GAHANNA CIVIC CENTER


CO-CREATE THE FUTURE

PROJECT OBJECTIVES


1. INVITING & APPROACHABLE
2. CREATE A CLEAR CIVIC PRESENCE
3. COMMUNITY & SERVICE FOCUSED
4. EFFICIENT IN PLANNING
5. ALLOW FOR FUTURE EXPANSION
6. SAFE & SECURE
7. MEETS ADDITION / RENOVATION SQ FT GOALS
8. MEETS PROGRAM GOALS
9. BUILDING RE-BRANDING / UNIQUE IDENTITY
10. DAYLIGHTING / QUALITY OF INTERIOR SPACES

Training Facility and Storm Shelter



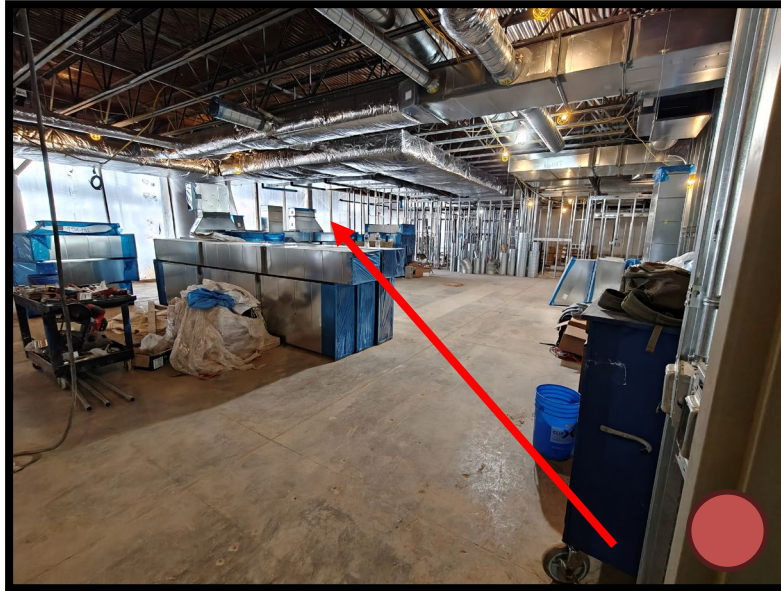


Police Training Room

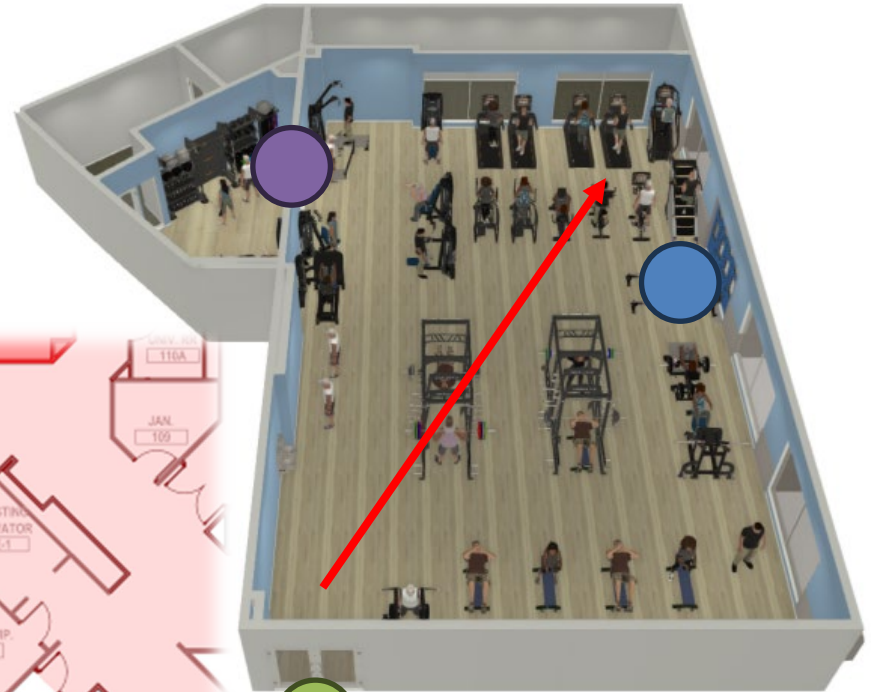



Fitness Center




Defense Tactics

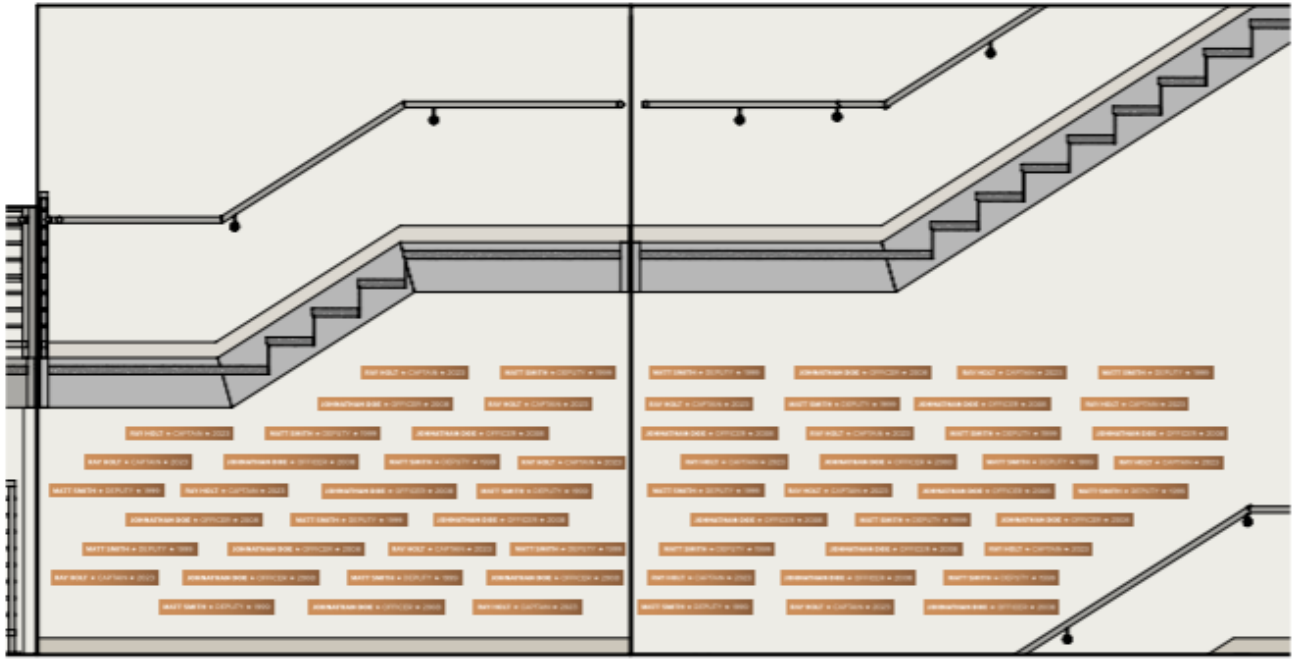

Internal Police Staircase

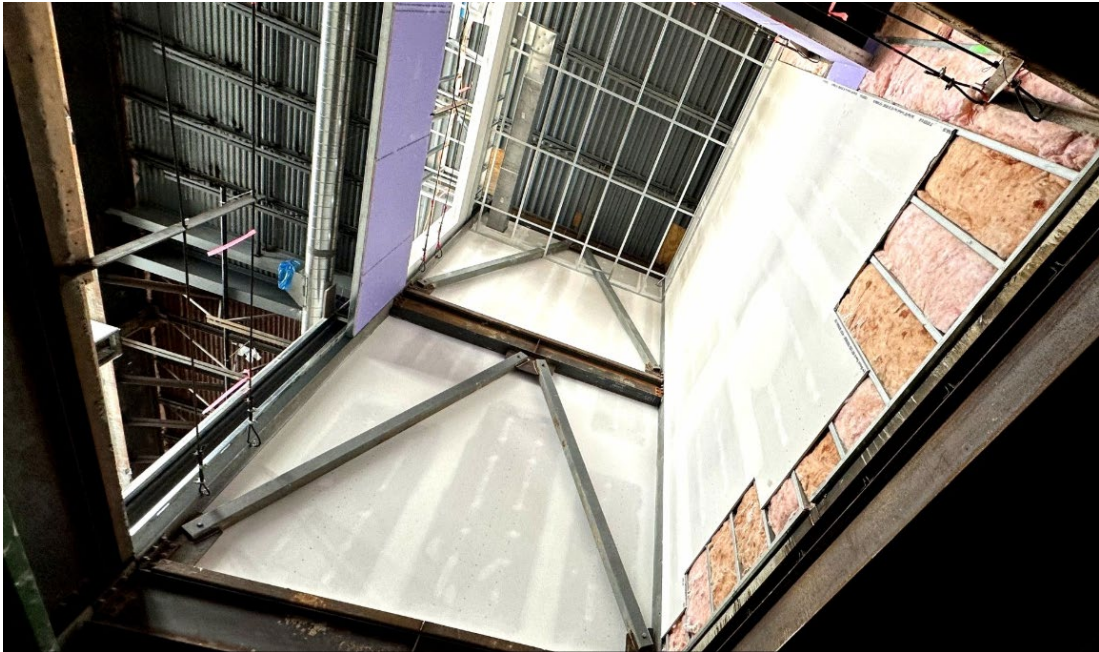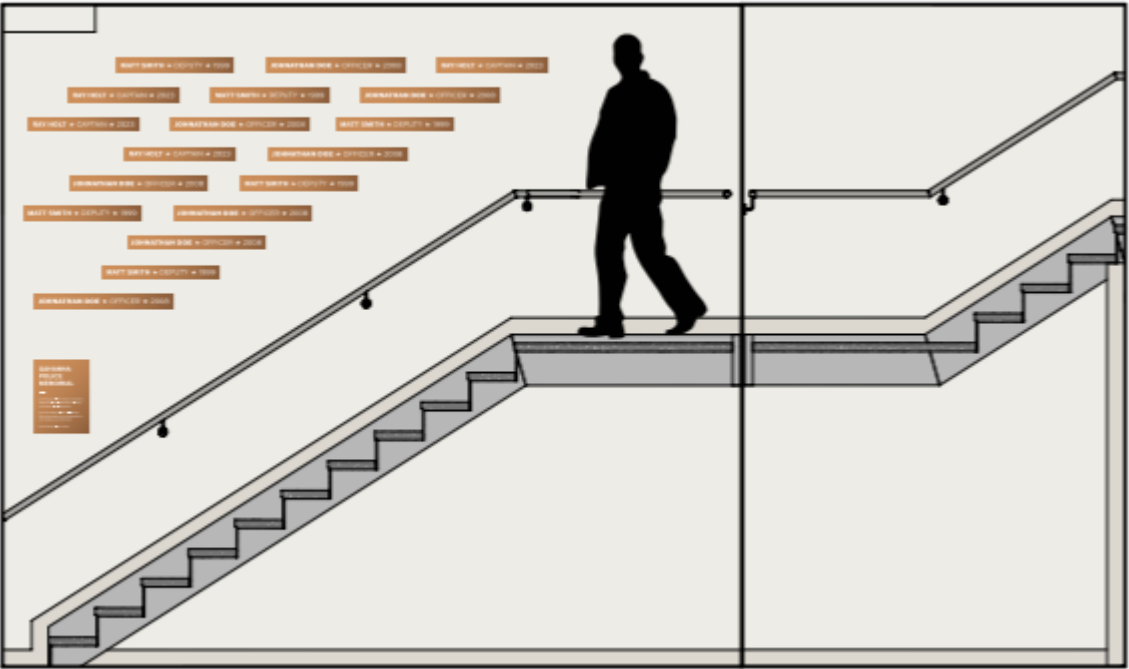

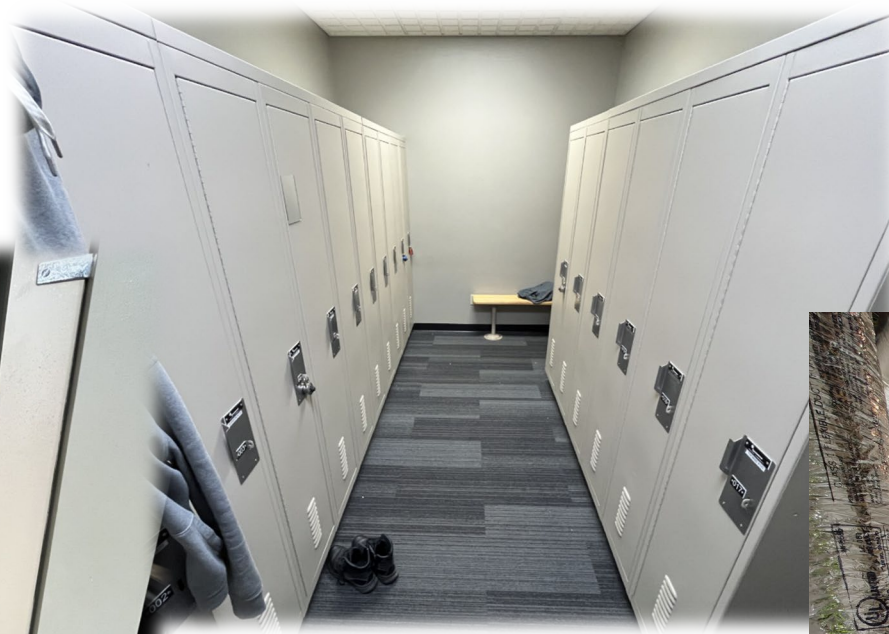

Existing Facility



Existing Facility



New Female Police
Locker Room



Early 2026

GAHANNA CIVIC CENTER

CO-CREATE THE FUTURE



MSA

DESIGN



April 14, 2025
