

PROJECT OBJECTIVES

- 1. INVITING & APPROACHABLE
- 2. CREATE A CLEAR CIVIC PRESENCE
- 3. COMMUNITY & SERVICE FOCUSED
- 4. EFFICIENT IN PLANNING
- 5. ALLOW FOR FUTURE EXPANSION
- 6. SAFE & SECURE
- 7. MEETS ADDITION / RENOVATION SQ FT GOALS
- 8. MEETS PROGRAM GOALS
- 9. BUILDING RE-BRANDING / UNIQUE IDENTITY
- 10. DAYLIGHTING / QUALITY OF INTERIOR SPACES































June-July Updates

Exterior


- Front Curbs and Police Egress Completed
- Solar Carport Footers Placed
- Bioswale Stormwater Facility Completed
- Asphalt Parking Lot Initial Course
- Rear Lot Site Work Begun
- Sidewalks & Multiuse Path

Interior

- Casework Installation 2nd & 3rd Floors
- Bathroom Finishes 3rd Floor
- Carpet & LVT Flooring 3rd Floor
- Building UPS Installed
- Room Controls, Lighting 2nd Floor
- First Floor Drywall

Schedule

- 73% Complete Based on Time
- 34 Weather Days

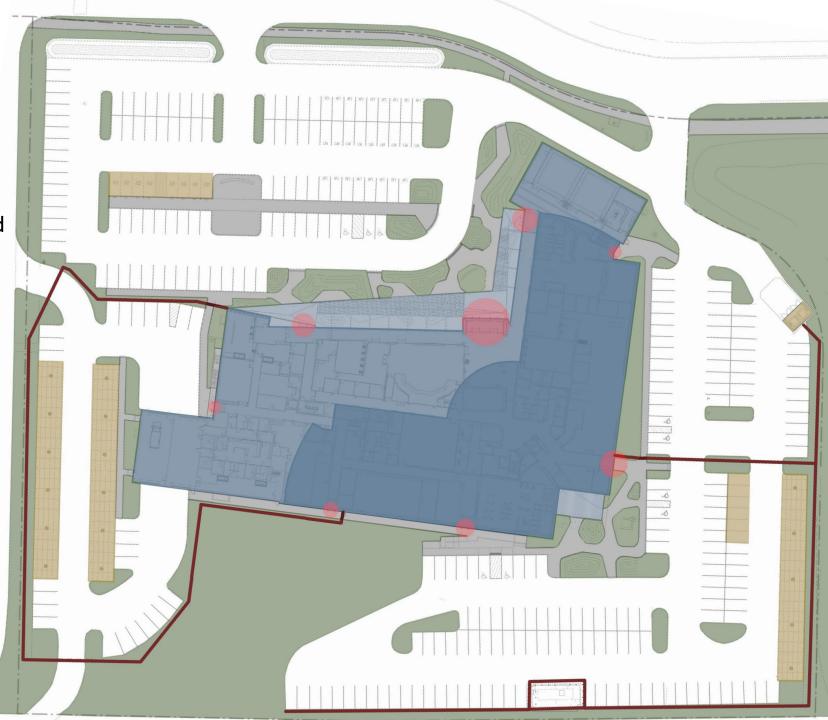





June-July Updates

Exterior

- Front Curbs and Police Egress Completed
- Solar Carport Footers Placed
- Bioswale Stormwater Facility Completed
- Asphalt Parking Lot Initial Course
- Rear Lot Site Work Begun
- Sidewalks & Multiuse Path

Interior

- Casework Installation 2nd & 3rd Floors
- Bathroom Finishes 3rd Floor
- Carpet & LVT Flooring 3rd Floor
- Ceiling Grid, HVAC Diffusers 2nd Floor
- Room Controls, Lighting 2nd Floor
- First Floor Drywall

Schedule

- 73% Complete Based on Time
- 34 Weather Days







July 25, 2024



July 23, 2025








July Financial Updates

Summary	
GMP1	\$20,237,613
GMP2	\$39,300,242
Total	\$59,627,855
Invoiced (61%)	\$36,486,225

Budgeted Allowance & Contingencies	
Allowances (52%)	\$1,054,700
Contingencies (53.3%)	\$3,722,194
Total	\$4,776,894
Approved (52.95%)	\$2,529,577

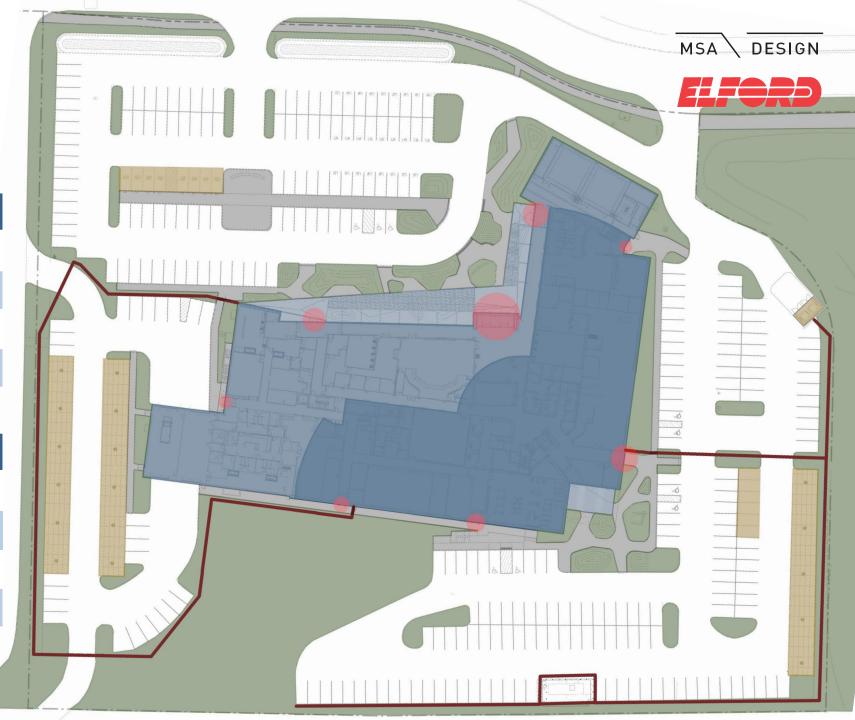



PROJECT OBJECTIVES

- 1. INVITING & APPROACHABLE
- 2. CREATE A CLEAR CIVIC PRESENCE
- 3. COMMUNITY & SERVICE FOCUSED
- 4. EFFICIENT IN PLANNING
- 5. ALLOW FOR FUTURE EXPANSION
- 6. SAFE & SECURE
- 7. MEETS ADDITION / RENOVATION SQ FT GOALS
- 8. MEETS PROGRAM GOALS
- 9. BUILDING RE-BRANDING / UNIQUE IDENTITY
- 10. DAYLIGHTING / QUALITY OF INTERIOR SPACES







